

Implementation Plan Lessons Learned

TOC-PLM-04 · status 09/30/2026 · internal working document, not controlled

Purpose / Scope:

Timing and action plan to capture lessons from projects, changes, problem solving, complaints and audits, prove their effectiveness and feed them into new projects. Standards: IATF 16949 7.1.6, 10.2.3, 10.3; VDA 6.3 P2.

Owner / involved:

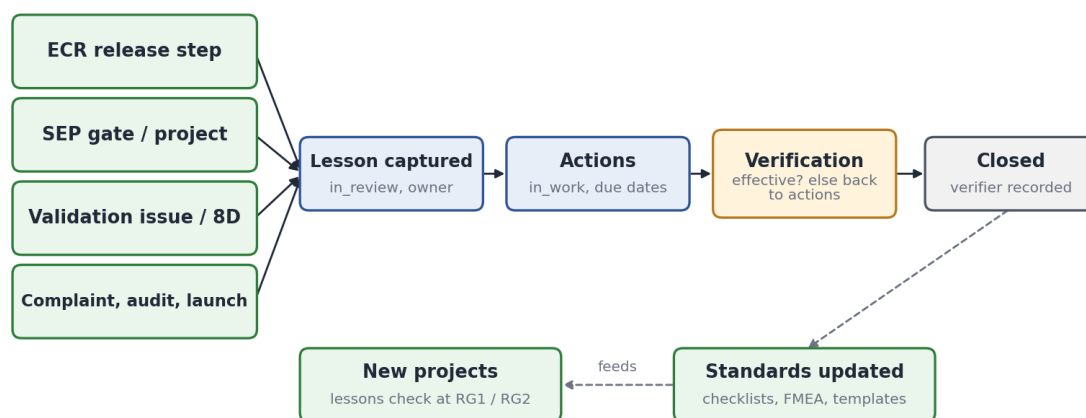
- C. Demmler, Process Development: owner of PLM2 and of every action in this plan, author, keeps it current
- Program Management and APQP: support (specification, tests, pilots on the running projects, evidence)
- Departments named per action (IT, Quality, Development, Tooling, HR, department heads): support where their part is needed
- Plant Management: monthly status review

1. Summary

Lessons learned are **built in PLM2** with owner, actions and a required effectiveness proof before closing. The SharePoint lessons list (LL-0001 to LL-0019, including ten G6X lessons) is already mirrored. The remaining step is to **bind lessons into the processes**: checked at SEP RG1/RG2, required at every change release and used as input to risk assessment. Procedure release is **01/04/2027**.

2. Requirements and how they are met

Requirement	How it is met	What we show
Organisational knowledge (7.1.6)	Central lessons database, filtered by project, category, department and tag	Lessons board
Problem solving uses lessons learned (10.2.3)	Lessons carry root cause and recommendation and are linked to the change or project they come from	Lesson with change link
Continual improvement (10.3)	Status flow with actions; closing needs effectiveness note and verifier	Closed lesson
Lessons from previous projects used (VDA 6.3 P2)	Lessons check recorded per project and gate	Lesson reference on project 1994

3. Process flow

Implementation Plan Lessons Learned

TOC-PLM-04 · status 09/30/2026 · internal working document, not controlled

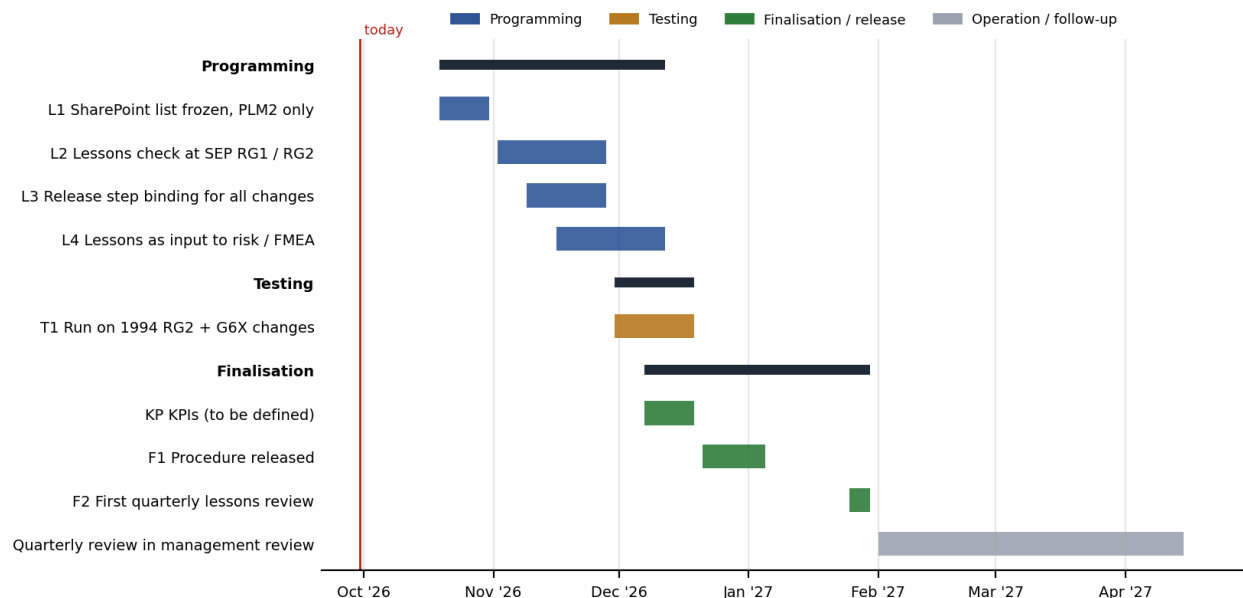
- Status: in review, in work, verification, closed (or rejected with category). A lesson cannot close while an action is open or without an effectiveness note.
- Stale lessons are flagged: 14 days in review, 7 days in verification; actions appear in the owner's task list.
- Closed lessons update standards (checklists, FMEA, templates) and are checked by the next projects at RG1 and RG2.

4. Where we stand today

Element	Status	Evidence in PLM2
Lessons with owner, actions, files, comments	Built	Lessons board and KPI board
Effectiveness proof and verifier before closing	Built	Close dialog
SharePoint list mirrored (LL-0001..0019)	Done	Live system, G6X lessons
Lessons step at change release	Built	Release tab of a change
Lessons check at SEP gates, input to risk / FMEA	Programming	Actions L2, L4

5. Tightening points

Today	Tightening measure	Action	Due
Lessons also kept in the SharePoint list	List frozen read-only; PLM2 only	L1	10/30/2026
Reuse in new projects is voluntary	Lessons check is a required SEP item at RG1 and RG2	L2	11/27/2026
Release lessons step can be skipped for small changes	Lessons step required for every change release	L3	11/27/2026
Lessons not linked to risk assessment	Relevant lessons listed in the project risk assessment	L4	12/11/2026

6. Timing and action plan

Implementation Plan Lessons Learned

TOC-PLM-04 · status 09/30/2026 · internal working document, not controlled

No.	Action	Phase	Owner	Support	Due	Done when
L1	SharePoint lessons list frozen read-only; PLM2 only	Programming	C. Demmler	Program Mgmt., APQP	10/30/2026	List locked
L2	Lessons check as required SEP item at RG1 / RG2	Programming	C. Demmler	Program Mgmt., APQP	11/27/2026	Item enforced in SEP
L3	Lessons step required at every change release	Programming	C. Demmler	Program Mgmt., APQP	11/27/2026	Release blocked in test
L4	Relevant lessons shown in project risk assessment	Programming	C. Demmler	Quality	12/11/2026	Risk form shows lessons
T1	Run on 1994 RG2 and the G6X changes	Testing	C. Demmler	Program Mgmt., APQP	12/18/2026	References recorded
KP	KPIs (open, to be defined): set targets, sources and review cycle for lessons learned, starting with lesson actions implemented on time	Finalisation	C. Demmler	Quality, Program Mgmt.	12/18/2026	KPI set agreed, shown in the monthly review
F1	Procedure 'Lessons learned in PLM2' released	Finalisation	C. Demmler	Quality	01/04/2027	Procedure in document control
F2	First quarterly lessons review in management review	Finalisation	C. Demmler	Plant Mgmt.	01/29/2027	Minutes filed

The table is the plan as of the status date above. Progress is tracked in the action plan **TOC-PLM-LOP (KTU LOP F-DVS-CORP-010)**; a date that moves is changed there with the reason, and this document is updated with it.

7. Control until go-live

Lessons are captured in PLM2 from now on. The SharePoint list stays readable as history until it is frozen (L1).

8. Effectiveness indicators

Indicator	Target	Source
Lessons closed with effectiveness proof	100 %	Lessons KPI board
New projects with lessons check at RG1 / RG2	100 %	SEP matrix
Lessons stale beyond flag limits	0 at monthly review	Lessons KPI board
Lesson actions implemented on time (due date met)	To be defined (action KP)	Lessons KPI board, due vs closed date

The KPI set beyond these indicators is to be defined (action KP): targets, data source in PLM2 and the review cycle are agreed with Quality and Program Management before the procedure is released.
