

Purpose / Scope:

Timing and action plan to run every product, process, tool and gauge change at KTX Toccoa in PLM2, including changes controlled by KTX Weissenburg. Standards: IATF 16949 8.5.6, 8.5.6.1, 8.3.6, 7.5.3; VDA 6.3 P2; VDA 2.

Owner / involved:

- C. Demmler, Process Development: owner of PLM2 and of every action in this plan, author, keeps it current
- Program Management and APQP: support (specification, tests, pilots on the running projects, evidence)
- Departments named per action (IT, Quality, Development, Tooling, HR, department heads): support where their part is needed
- Plant Management: monthly status review


1. Summary

The change process is **built and running in PLM2**. What remains is **testing with the departments and tightening the role model**, so that every step is done by the right function only. Go-live, meaning every new change at TOC runs in PLM2 only, is **12/21/2026**.

2. Requirements and how they are met

Requirement	How it is met	What we show
Documented change process, risk analysis before implementation (8.5.6, 8.5.6.1)	Fixed stages; routed departments assess with an impact checklist and typed risks; not feasible stops the change	Assessment tab of any change
Customer approval before implementation (8.3.6.1, 8.5.6.1)	Hard gate for customer changes: valid offer accepted plus PM and Quality sign-off before approved; internal changes need PM cost approval	Offer tab, sign-off record
Verification / validation of the change (8.5.6)	Validation stage with department checks, a 16-item release checklist and validation issues (8D, escalation L1-L3)	Release tab
Records and traceability (7.5.3)	Every action in a hash-chained audit trail; documents filed per stage	Changelog of the change
Changes from the mother plant	Weissenburg side track: impact lock by Development and read-and-understood receipts before approval	CR-2026-0001..0003 (G6X)


3. Process flow

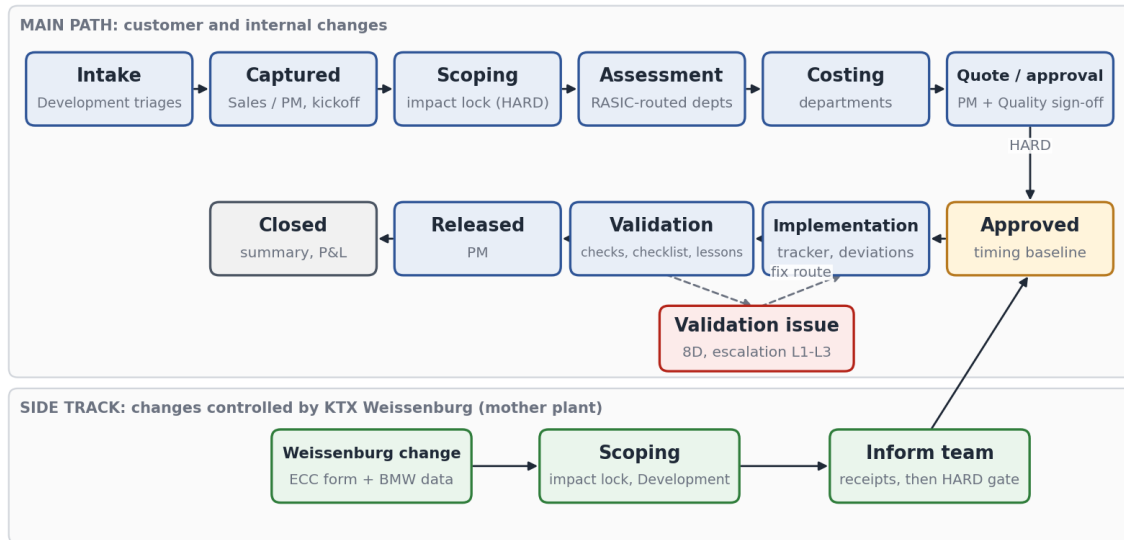

- **Hard gates** cannot be overridden by anyone: impact lock before assessment, customer acceptance with PM and Quality sign-off before approval, and for Weissenburg changes impact lock plus team informed.
- **Soft guards** (kickoff, timing validated, release checklist) can only be passed with a documented, approved deviation.
- **Routing** (R/A/S/C per department) is set at scoping; a department added later needs a reason and a second approver.

4. Timing planner and tasks

Timing tab: detailed plan of one change (schematic)

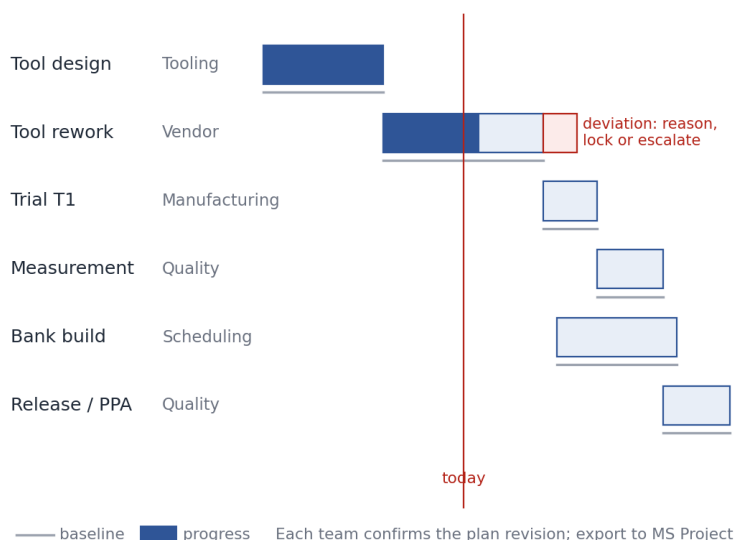

My tasks: what each person sees

Confirm plan revision 2 Tooling	due Thu
Progress report tool rework Tooling	due Tue
Release checklist: gauge check Quality	overdue
Decide plan deviation PM	due today
Read and understood: ECC-0013 Production	due Fri
Lessons learned step PM	next

Due-soon and overdue reminders go to the responsible, the backup of the department is informed

Implementation Plan Change Management (ECR)

TOC-PLM-01 · status 09/30/2026 · internal working document, not controlled

- **Timing planner:** every approved change gets a detailed plan with blocks per department and vendor. Each responsible team confirms the plan revision; 'timing validated' sets the baseline. Export to MS Project for the customer.
- **Tracking:** progress and actual dates per block, regular progress reports. After the baseline every date move is a deviation with a reason, accepted internally or escalated to the customer through Sales.
- **Tasks:** every person sees their own open tasks (confirm plan, answer assessment, report progress, release check, decide deviation, read and understood) with due dates in 'My tasks' and a next-step checklist on the change.
- **Reminders:** due-soon and overdue tasks and deadlines at risk are notified automatically; the project team has one responsible per role and a backup.


5. Where we stand today

Element	Status	Evidence in PLM2
Stages captured to closed, internal branch	Built	Lifecycle and gates in every change record
Assessment, costing, offer, negotiation	Built	Assessment, Costing and Offer tabs
Timing planner, baseline, deviations, tasks	Built	Timing tab, My tasks
Release checklist, lessons step, validation issues	Built	Release tab
Weissenburg side track	Built, in use	G6X changes CR-2026-0001..0003 from the ECC list
Department rights per function	Tightening	Actions E1-E3
Acceptance test with all departments	Testing	Actions T1-T2

6. Tightening points

Today	Tightening measure	Action	Due
Edit rights are broad: most editors hold the admin role	Rights per department from the company directory groups; admin only for IT and the system owner	E1	11/13/2026
Internal cost approval allows the requester to approve	Strict four-eyes on every approval and sign-off	E2	11/06/2026
Training is recorded but not required	Only trained users can act on a stage (training gate on)	E3	11/20/2026
Changes also kept in SharePoint ECC list and Excel form	PLM2 is the record from go-live; list frozen read-only	F3	12/21/2026

7. Timing and action plan

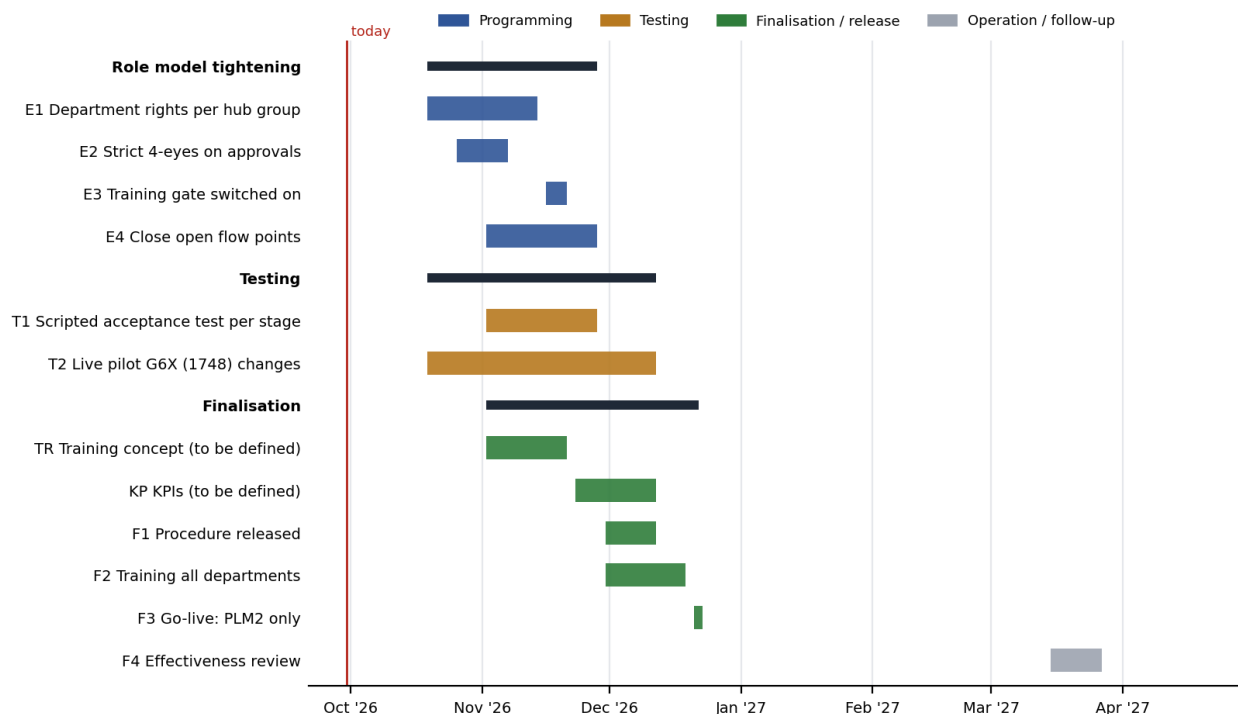

No.	Action	Phase	Owner	Support	Due	Done when
E1	Department rights from directory groups; admin role limited to IT and system owner	Programming	C. Demmler	IT	11/13/2026	Rights matrix filed; test log per role
E2	Strict four-eyes on internal cost approval and sign-offs	Programming	C. Demmler	Program Mgmt., APQP	11/06/2026	Self-approval rejected in test
E3	Training gate switched on per stage	Programming	C. Demmler	HR	11/20/2026	Untrained user blocked in test
E4	Close open flow points (cost carrier re-confirmation, impact edits after quote)	Programming	C. Demmler	Program Mgmt., APQP	11/27/2026	Regression suite green
T1	Scripted acceptance test, one script per stage, signed by each department	Testing	C. Demmler	Department heads	11/27/2026	Signed test protocols filed
T2	Live pilot: G6X (1748) Weissenburg changes plus the next customer change	Testing	C. Demmler	Program Mgmt., APQP	12/11/2026	Pilot changes complete in PLM2
KP	KPIs (open, to be defined): set targets, sources and review cycle for the change process, starting with implementation on time	Finalisation	C. Demmler	Quality, Program Mgmt.	12/11/2026	KPI set agreed, shown in the monthly review
F1	Procedure 'Change management with PLM2' released	Finalisation	C. Demmler	Quality	12/11/2026	Procedure in document control
TR	Training concept (open, to be defined): which roles need which training per module (ECR, SEP, data, lessons), format, trainer, records	Finalisation	C. Demmler	Program Mgmt., APQP, HR	11/20/2026	Concept agreed with department heads

Implementation Plan Change Management (ECR)

TOC-PLM-01 · status 09/30/2026 · internal working document, not controlled

No.	Action	Phase	Owner	Support	Due	Done when
F2	Training of all departments per training concept (TR)	Finalisation	C. Demmler	Program Mgmt., APQP	12/18/2026	Training records in PLM2
F3	Go-live: new changes in PLM2 only; ECC list read-only	Finalisation	C. Demmler	Plant Mgmt.	12/21/2026	Announcement; list locked
F4	Effectiveness review after three months	Operation	C. Demmler	Quality	03/26/2027	Review in management review

The table is the plan as of the status date above. Progress is tracked in the action plan **TOC-PLM-LOP (KTX LOP F-DVS-CORP-010)**; a date that moves is changed there with the reason, and this document is updated with it.

8. Control until go-live

Until 12/21/2026 the Weissenburg form GB-CM-0001 and the SharePoint ECC list stay valid. Every change they hold for TOC is also opened in PLM2 with the form filed on it, so the PLM2 record is complete from the first day of the pilot.

9. Effectiveness indicators

Indicator	Target	Source
Changes run outside PLM2 after go-live	0	ECC list (read-only) vs PLM2
Changes released with open validation issue	0	Release tab
Changes past release deadline	Trend down, reviewed monthly	Change list, deadline state
Overdue tasks at monthly review	Trend down	My tasks / notifications
Changes implemented on time (implementation date met)	To be defined (action KP)	Change list, implementation deadline vs actual

The KPI set beyond these indicators is to be defined (action KP): targets, data source in PLM2 and the review cycle are agreed with Quality and Program Management before go-live.
