

Implementation Plan Data Management and Traceability

TOC-PLM-03 · status 09/30/2026 · internal working document, not controlled

Purpose / Scope:

Timing and action plan for customer data, engineering levels, revisions and the part-tool-gauge-equipment relations of all KTX Toccoa projects in PLM2. Standards: IATF 16949 7.5.3, 7.5.3.2.1, 7.5.3.2.2, 8.5.2, 8.5.2.1.

Owner / involved:

- C. Demmler, Process Development: owner of PLM2 and of every action in this plan, author, keeps it current
- Program Management and APQP: support (specification, tests, pilots on the running projects, evidence)
- Departments named per action (IT, Quality, Development, Tooling, HR, department heads): support where their part is needed
- Plant Management: monthly status review


1. Summary

Traceability, engineering level and the data itself are already tight in PLM2: every part carries its revision history with engineering level and customer index, every change is written to a tamper-evident audit trail, and part, tool, gauge and equipment are linked as system data. The module is **in development** for the remaining functions below; go-live, meaning network drives become read-only for active projects, is **03/22/2027**.

2. Requirements and how they are met

Requirement	How it is met	What we show
Control of documented information (7.5.3)	One active revision per part; older revisions stay in the history, read-only	Part page, revision list
Engineering specifications, review of customer changes (7.5.3.2.2)	Every new customer index enters intake; Development decides: administrative, engineering review or full change	Intake list, decision with reason
Record retention (7.5.3.2.1)	Revisions are superseded, never overwritten; every data change in the audit trail; database backed up before every data operation	Revision history, backup log
Identification and traceability (8.5.2, 8.5.2.1)	Part numbers by family, tool and gauge numbering (tool-operation), relations with where-used and BOM	Where-used of a tool, e.g. 3360

3. Process flow

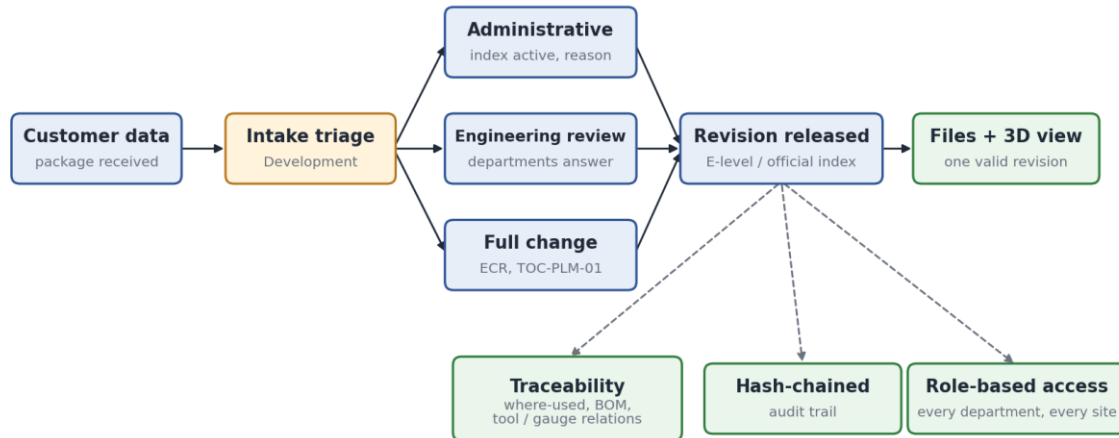

- **Levels:** E1, E2 = customer review data; 1, 2 = official customer data; x.1 = own proposal. Shown as 'E2 · B' (our level · customer index). Counters never reset, so every level is unique.
- **Relations:** a tool produces articles, a gauge checks them, equipment serves the tool; mirror parts are relations, never copies.
- **Legacy data:** the former system (WinCarat) was imported once and is read-only; PLM2 is the master since.


4. Where we stand today

Element	Status	Evidence in PLM2
Revision and level scheme, customer package receive	Built, tight	Part page of any series part
Hash-chained audit trail on parts and changes	Built, tight	Part changelog
Relations part-tool-gauge-equipment, where-used, BOM	Built, tight	1,337 tool-article links; 152 gauges and 14 equipment linked
3D view of customer data (STEP)	Built	Viewer on the revision
Review deadline for customer data (10 working days)	In development	Action M2
Completeness: gauges without tool, customer part numbers	In development	Actions M3-M4
Access scope on every list	In development	Action M1

5. Tightening points

Today	Tightening measure	Action	Due
Drawings and customer data partly still on network drives	Transfer per active project; drives read-only after go-live	M6, F2	03/22/2027
Review time of customer data not measured	Intake timer with overdue signal at 10 working days	M2	11/27/2026
Some records incomplete (gauges without tool, customer part numbers)	Completeness list, closed per project	M3, M4	01/04/2027
Backup before data operations, not yet scheduled	Scheduled backup with documented restore test	M5	11/20/2026

6. Timing and action plan

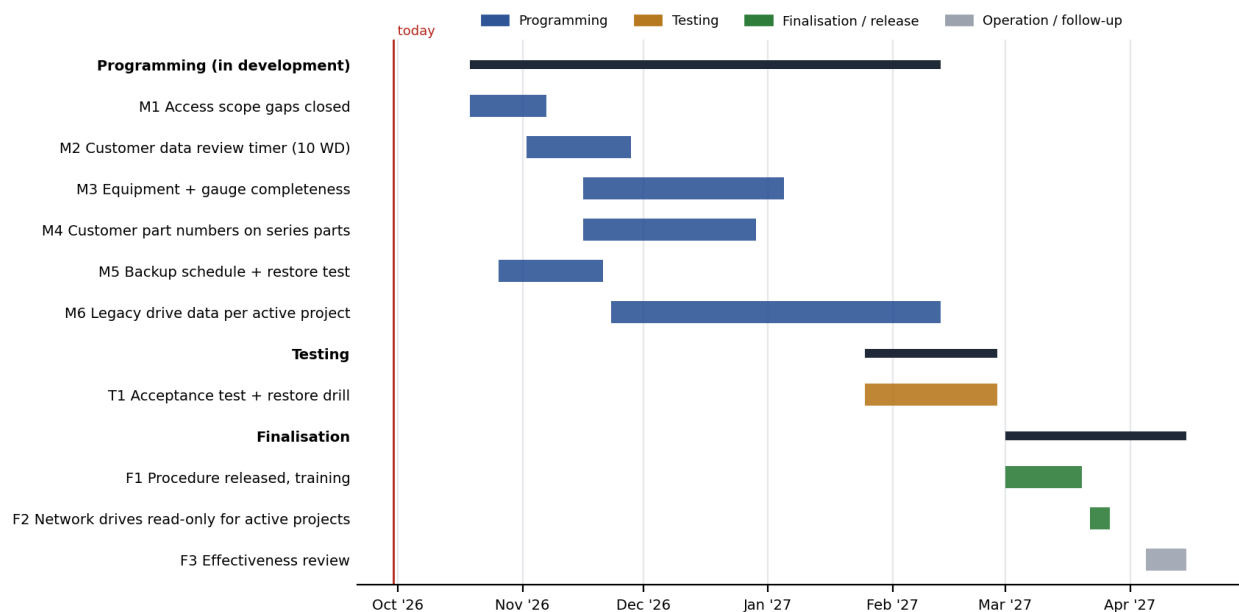

No.	Action	Phase	Owner	Support	Due	Done when
M1	Access scope closed on all lists (SEP, lessons)	Programming	C. Demmler	Program Mgmt., APQP	11/06/2026	Scope test per role passed
M2	Customer data review timer, 10 working days, overdue signal	Programming	C. Demmler	Development	11/27/2026	Timer on intake list
M3	Equipment and gauge completeness (tool link, equipment details)	Programming	C. Demmler	Tooling, Quality	01/04/2027	0 gauges without tool
M4	Customer part numbers on all series parts; one mirror per part	Programming	C. Demmler	Development	12/28/2026	Completeness list empty
M5	Scheduled database backup and restore test	Programming	C. Demmler	IT	11/20/2026	Restore test record
M6	Transfer legacy drive data of active projects	Programming	C. Demmler	Development	02/12/2027	Per-project checklist signed
T1	Acceptance test and restore drill	Testing	C. Demmler	Quality, IT	02/26/2027	Signed test protocol
F1	Procedure 'Engineering data management in PLM2' released, training	Finalisation	C. Demmler	Quality	03/19/2027	Procedure; training per concept (TOC-PLM-01 TR)
F2	Network drives read-only for active projects	Finalisation	C. Demmler	IT	03/22/2027	Drive rights changed
F3	Effectiveness review	Operation	C. Demmler	Quality	04/14/2027	Review in management review

The table is the plan as of the status date above. Progress is tracked in the action plan **TOC-PLM-LOP (KTX LOP F-DVS-CORP-010)**; a date that moves is changed there with the reason, and this document is updated with it.

Implementation Plan Data Management and TraceabilityTOC-PLM-03 · status 09/30/2026 · internal working document, not controlled

7. Control until go-live

Until 03/22/2027 the valid revision of a part is the one released in PLM2; files still on drives are reference copies. New customer data is received in PLM2 only.

8. Effectiveness indicators

Indicator	Target	Source
Customer data reviewed within 10 working days	100 %	Intake list
Parts / tools / gauges with incomplete data	0 for active projects	Completeness list
Successful restore tests	1 per quarter	IT backup log
