

Purpose / Scope:

Timing and action plan to run project planning with the SEP matrix (maturity gates RG1-RG7) in PLM2 for all customer projects from RFQ to series. Standards: IATF 16949 8.3.2, 8.3.2.1, 8.3.4, 8.3.4.4; VDA MLA; VDA 6.3 P2-P4.

Owner / involved:

- C. Demmler, Process Development: owner of PLM2 and of every action in this plan, author, keeps it current
- Program Management and APQP: support (specification, tests, pilots on the running projects, evidence)
- Departments named per action (IT, Quality, Development, Tooling, HR, department heads): support where their part is needed
- Plant Management: monthly status review


1. Summary

The SEP matrix is **fully in PLM2**: seven maturity gates with 232 items, the same content as the group template GB-DP-0001, created for every project. What remains is **uploading the evidence** of the running projects. Project **1994 (Brose Seat Trim, nominated 09/21/2026)** is the lead project: it runs every gate in PLM2 up to SOP, and the rules tighten with it. From **01/18/2027** new projects start in PLM2 only.

2. Requirements and how they are met

Requirement	How it is met	What we show
Design and development planning, multidisciplinary (8.3.2, 8.3.2.1)	SEP matrix per project; every item has a responsible function and a status (open, done, not applicable)	SEP tab of project 1994
Monitoring at defined stages (8.3.4)	Gates close in order; closing needs PM and Quality sign-off and locks the items	Gate status, sign-off record
Product approval process (8.3.4.4)	Pre-series gate B/RG6 and series gate A/RG7 carry the approval items	Gates RG6 / RG7
Documented evidence	Files attached per SEP item; every item change audited field by field	Documents tab, item history
Maturity level logic (VDA MLA)	Gates K0/RG1 to A/RG7 follow the maturity levels	SEP matrix

3. Process flow

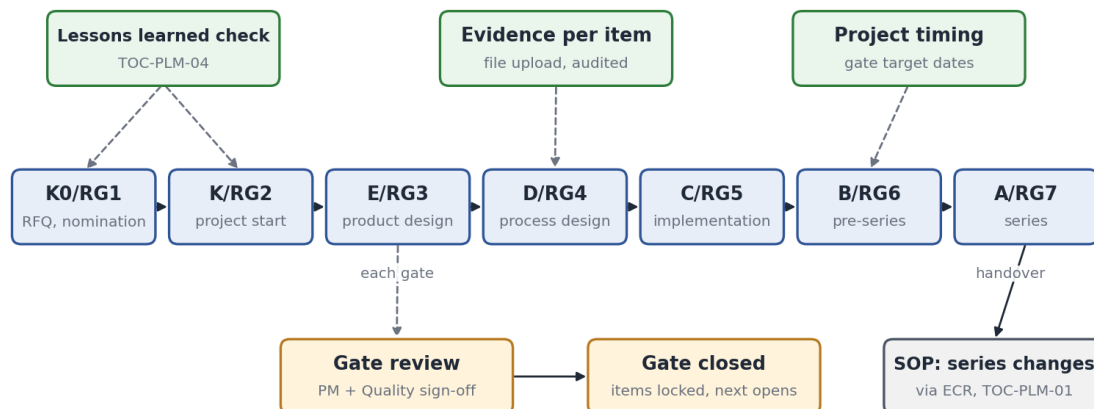

- A gate opens only after the previous one is closed. Items are done or marked not applicable with a reason; nothing is skipped silently.
- Lessons learned are checked at RG1 and RG2 (TOC-PLM-04); evidence is filed on the item it proves.
- At SOP (A/RG7) the project hands over to series: from then on every change runs through TOC-PLM-01.

4. Project overview

A **project overview page** (action S1) shows every active project on one screen: current gate, gate target date, items open and overdue, open changes and open lessons. It is the page used in the monthly review and shown first in an audit. SEP items with an owner and due date appear in the owner's task list like change tasks (TOC-PLM-01, section 4).

5. Where we stand today

Element	Status	Evidence in PLM2
SEP matrix, 7 gates / 232 items per project	Built	Projects 1864, 1994, 2141, 2277
Dual sign-off and item lock at gate close	Built	Gate close dialog
File evidence per item, field audit	Built	Documents tab, item history
Standard forms (risk assessment, handover, legitimisation, contact list, LOP, deviation agreement)	Built	Forms tab
Evidence of running projects uploaded	In progress	Actions D1-D2
Gate target dates, project overview, item enforcement	Programming	Actions S1-S3

6. Tightening points

Today	Tightening measure	Action	Due
Evidence still on drives and in the Excel matrix	Upload per item for running projects; Excel frozen for new projects	D1, F2	01/18/2027
Gate dates not yet in the system	Target date per gate with overdue signal, linked to the project timing	S2	11/13/2026

Today	Tightening measure	Action	Due
Required items per gate not enforced	Gate cannot close while a required item is open; defined signer per item	S3	12/11/2026
No single view across projects	Project overview page	S1	11/20/2026

7. Timing and action plan



No.	Action	Phase	Owner	Support	Due	Done when
S1	Project overview page (all projects, gates, overdue, open changes and lessons)	Programming	C. Demmler	Program Mgmt., APQP	11/20/2026	Page live, used in monthly review
S2	Gate target dates linked to project timing, overdue signal	Programming	C. Demmler	Program Mgmt., APQP	11/13/2026	Dates set for all running projects
S3	Required items per gate enforced; signer role per item	Programming	C. Demmler	Quality	12/11/2026	Gate close blocked in test
D1	Upload SEP evidence for running projects (1864, 1994, 2141, 2277)	Documentation	C. Demmler	Program Mgmt., APQP	01/04/2027	Items done / n.a. with evidence
D2	1994: RG1 evidence complete, gate review with dual sign-off	Documentation	C. Demmler	Quality	12/04/2026	RG1 closed in PLM2
F1	Procedure 'Project planning with the SEP matrix in PLM2' released	Finalisation	C. Demmler	Quality	12/28/2026	Procedure in document control
F2	Excel SEP matrix retired for new projects	Finalisation	C. Demmler	Plant Mgmt.	01/18/2027	First new project started in PLM2
R1	1994 runs RG2 to RG7 in PLM2; gate dates from the Brose customer timing	Operation	Program Mgmt.	to SOP	Each gate closed with sign-off	

The table is the plan as of the status date above. Progress is tracked in the action plan **TOC-PLM-LOP (KTX LOP F-DVS-CORP-010)**; a date that moves is changed there with the reason, and this document is updated with it.

8. Control until go-live

Running projects keep their current SEP evidence valid while it is uploaded; the upload is tracked item by item in PLM2, so the open amount is visible at any time. Project 1994 runs in PLM2 from now on.

9. Effectiveness indicators

Indicator	Target	Source
Gates closed on or before target date	90 %	Project overview
Required items closed without evidence file	0	SEP matrix
New projects started outside PLM2 after 01/18/2027	0	Project list
